Ashton Town Hall - H&S Works
Tender Submission Programme

Line	Name	Start	Finish	Duration (Working Weeks)
	Ashton Town Hall - Pre-construction & Mobilisation	**11/12/2023**	**15/04/2024**	**15w 3d**
2	RCG Market Testing / Gateway 2	11/12/2023	19/01/2024	4w
3	Submit High Level Programme & Costs To Client	22/01/2024	22/01/2024	
4	Client Review High Level Cost & Programme	22/01/2024	31/01/2024	1w 3d
5	Comercial Discusssion / Negotiations / Gateway 3	22/01/2024	23/02/2024	5w
6	Contract Discussions / Negotiations	01/02/2024	23/02/2024	3w 2d
7	Contract Award	23/02/2024	23/02/2024	
8	Mobilisation Period / Commence Procurement	26/02/2024	12/04/2024	6w 3d
9	Start On Site	15/04/2024	15/04/2024	
	Procurement: Long Lead in Items - Stone	**26/02/2024**	**08/07/2024**	**18w 1d**
11	**Stonework**	**26/02/2024**	**08/07/2024**	**18w 1d**
12	Long Lead in Items: Stonework: Raise Order / TCI / Directors Sign Off	26/02/2024	15/03/2024	3w
13	Place Order With Clan for Stonework's	18/03/2024	18/03/2024	
14	Lead in / Manufacture: Stonework: Raise Order / TCI / Directors Sign Off	18/03/2024	31/05/2024	10w 1d
15	Stonework's Starts On Site	08/07/2024	08/07/2024	
	LBC Approval Period	**22/01/2024**	**07/06/2024**	**19w 1d**
17	LBC 02 Approval Period - Scaffold & Further Surveys	22/01/2024	12/04/2024	11w 3d
18	LBC 03 Design Development	22/01/2024	08/03/2024	7w
19	LBC 03 Approval Period - Stoneworks / Masonry etc.	11/03/2024	07/06/2024	12w 1d
	Temporay Works Desin (Scaffoldding)	**11/03/2024**	**05/04/2024**	**3w 3d**
21	Scaffold Design / Temporay Works Desin (Scaffoldding)	11/03/2024	05/04/2024	3w 3d
	Ashton Town Hall - H&S Works	**15/04/2024**	**20/12/2024**	**35w 2d**
23	**Site Set Up / Erect Scaffolding**	**15/04/2024**	**05/07/2024**	**11w 3d**
24	Site Set Up / Site Establishment	15/04/2024	10/05/2024	3w 4d
25	Erect Perimeter Scaffolding / Butresses / Erect Haki Stairs / Hoist	07/05/2024	05/07/2024	8w 3d
26	**Parapet & Facade Works**	**08/07/2024**	**13/12/2024**	**22w 4d**
27	SAMPLE PANEL - Parapet Deconstruction / Rebuild With New Elements	08/07/2024	19/07/2024	2w
28	Stone Condition Survey Of Parapet & Full Stone Elevation	22/07/2024	26/07/2024	1w
29	South, East & West Elevations - Parapet Deconstruction / Rebuild With New	29/07/2024	06/09/2024	5w 4d
30	TBC - Works To Facade / Removal Of Ferrous Metal Fixings	09/09/2024	01/11/2024	8w
31	Remove Perimeter Scaffolding	04/11/2024	13/12/2024	6w
32	**Decant From Site**	**16/12/2024**	**20/12/2024**	**1w**
33	Decant From Site	16/12/2024	20/12/2024	1w
34	PC	20/12/2024	20/12/2024	

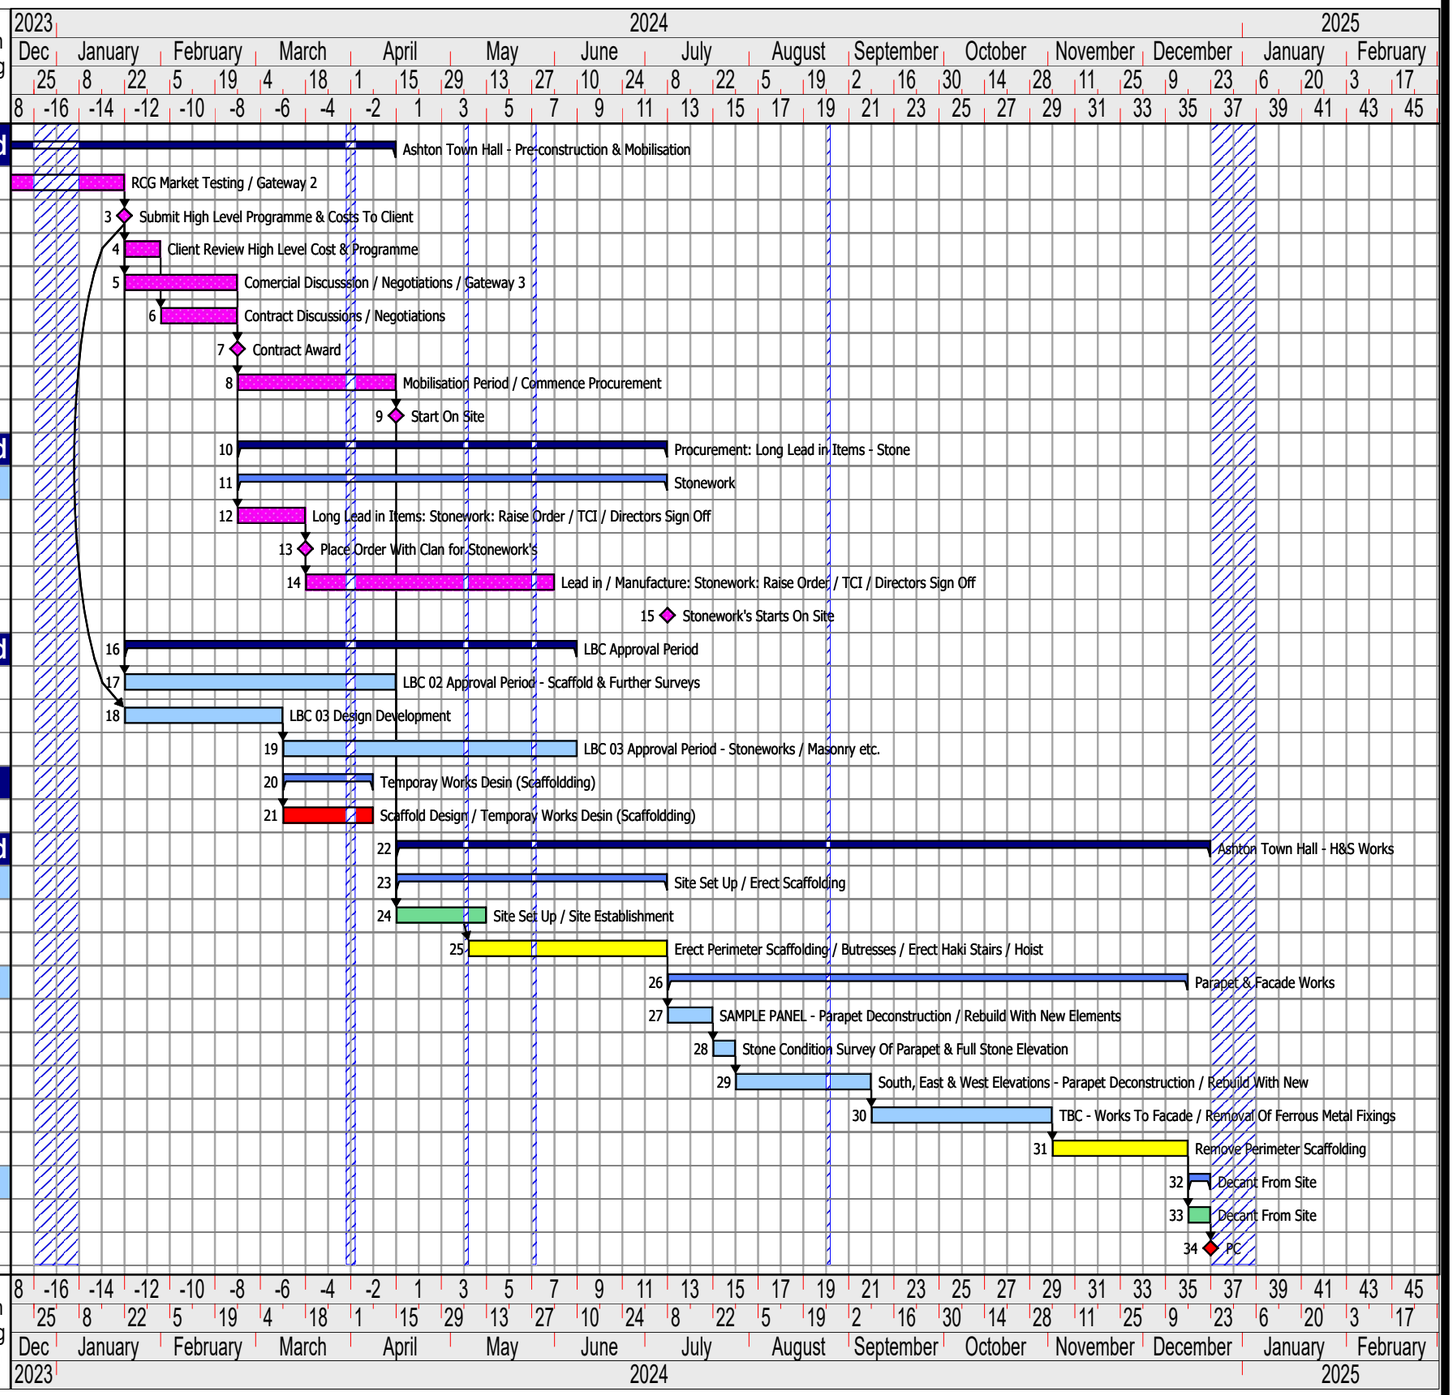

Robertson Construction Group
3 The Parks
Haydock
Newton Le Willows
Merseyside WA12 oJQ
TEL: 01942 590910

PROGRAMME No : ATH H&S - CP04
PROGRAMME STATUS : Tender Submission: 15.01.24
CHART AUTHOR : Robertson Planning Dept

Rev: 04 (15/01/24)
